



































































ID		Task Mode	Task Name	Duration	Start
1			1 Rail Loop Foundation Design & Permitting	383 days	Tue 9/1/20
2			1.1 Task Order Issued	0 days	Tue 9/1/20
3			1.2 Field Investigation	19 days	Mon 9/14/20
4			1.2.1 Topographic Survey & Wetland Flag Survey	1 wk	Mon 9/14/20
5			1.2.2 Geotechnical Investigation	2.2 wks	Thu 9/24/20
6			1.3 Lab Testing & Geotechnical Report	8 wks	Fri 10/9/20
7			1.4 Refine Foundation Options & Costs	60 days	Fri 12/4/20
8			1.4.1 Refine Foundation Options, Wetland Impact & Cost	5 wks	Fri 12/4/20
9			1.4.2 Review with DRP & Select Preferred Foundation Options Along Alignment	7 wks	Fri 1/8/21
10			1.5 Prepapre Preliminary Foundation Design	8 wks	Fri 2/26/21
11			1.6 Prepare NJDEP Combined WD/FHA/CW/FWW Permit Applications	110 days	Fri 1/8/21
12			1.6.1 Pre-Application Meeting	0 days	Tue 3/2/21
13			1.6.2 Prepare Permit Drawings	7 wks	Fri 3/19/21
14			1.6.3 Submit to CONRAIL for Review/Approval	5 wks	Fri 5/7/21
15			1.6.4 Prepare Application Items	100 days	Fri 1/8/21
16			1.6.4.1 Alternatives Analysis	5 wks	Fri 1/8/21
17			1.6.4.2 Compliance Statement/EIS	11 wks	Fri 1/8/21
18			1.6.4.3 Public Notice/Admin Items	3 wks	Fri 3/26/21
19			1.6.4.4 Client/Counsel Review	3 wks	Fri 3/26/21
20			1.6.4.5 Finalize Application	3 wks	Fri 5/7/21
21			1.6.4.6 Submit Application	0 days	Thu 5/27/21
22			1.7 NJDEP Permit Application Review & Apporval	190 days	Fri 5/28/21
23			1.7.1 Completeness Review (20 Working days)	20 days	Fri 5/28/21








Project: Implementation Schedu
Date: Fri 5/21/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	






















ID		Task Mode	Task Name	Duration	Start
24			1.7.2 Technical Review (90 days + 30 days extension)	6 mons	Fri 6/25/21
25			1.7.3 Permit Issued (Note FWW not limited to 90-days review)	2.5 mons	Fri 12/10/21
26			2 Construction	195 days	Fri 2/18/22
27			2.1 Survey and Finalize track layout	4 wks	Fri 2/18/22
28			2.2 Shop drawing Prep	6 wks	Fri 2/18/22
29			2.3 Procurement	90 days	Fri 4/1/22
30			2.3.1 Sub-ballast	2 wks	Fri 4/1/22
31			2.3.2 Ballast	2 wks	Fri 4/1/22
32			2.3.3 Ties	4 wks	Fri 4/1/22
33			2.3.4 Industrial Turnouts (Fabricate & Delivery)	90 days	Fri 4/1/22
34			2.3.5 Rails 10,000 ft x 2	60 days	Fri 4/1/22
35			2.3.6 Signals	30 days	Fri 4/1/22
36			2.3.7 Crossings	30 days	Fri 4/1/22
37			2.4 Civil	40 days	Fri 2/18/22
38			2.4.1 Clearing and surface prep.	3 wks	Fri 2/18/22
39			2.4.2 Piles driving	5 wks	Fri 3/11/22
40			2.4.3 Grade and drainage	4 wks	Fri 2/18/22
41			2.5 Rail Installation	175 days	Fri 3/18/22
42			2.5.1 Subgrade/Sub-ballast	4 wks	Fri 4/15/22
43			2.5.2 Ballast	3 wks	Fri 5/13/22
44			2.5.3 Ties installtion	10 days	Fri 6/3/22
45			2.5.4 Rails layout at rate of 300 ft/day	70 days	Fri 6/24/22
46			2.5.5 Stream cross over (2)	8 wks	Fri 3/18/22


Project: Implementation Schedu
Date: Fri 5/21/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

ID		Task Mode	Task Name	Duration	Start
47			2.5.6 Industrial Turnouts	1 wk	Fri 8/5/22
48			2.5.7 Lighting	6 wks	Fri 3/18/22
49			2.5.8 2 weeks	2 wks	Fri 9/30/22
50			2.5.9 Crossings	2 wks	Fri 6/17/22
51			2.5.10 Alignment & Tampering	4 wks	Fri 9/30/22
52			2.5.11 Top ballast	3 wks	Fri 10/28/22


Project: Implementation Schedu
Date: Fri 5/21/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

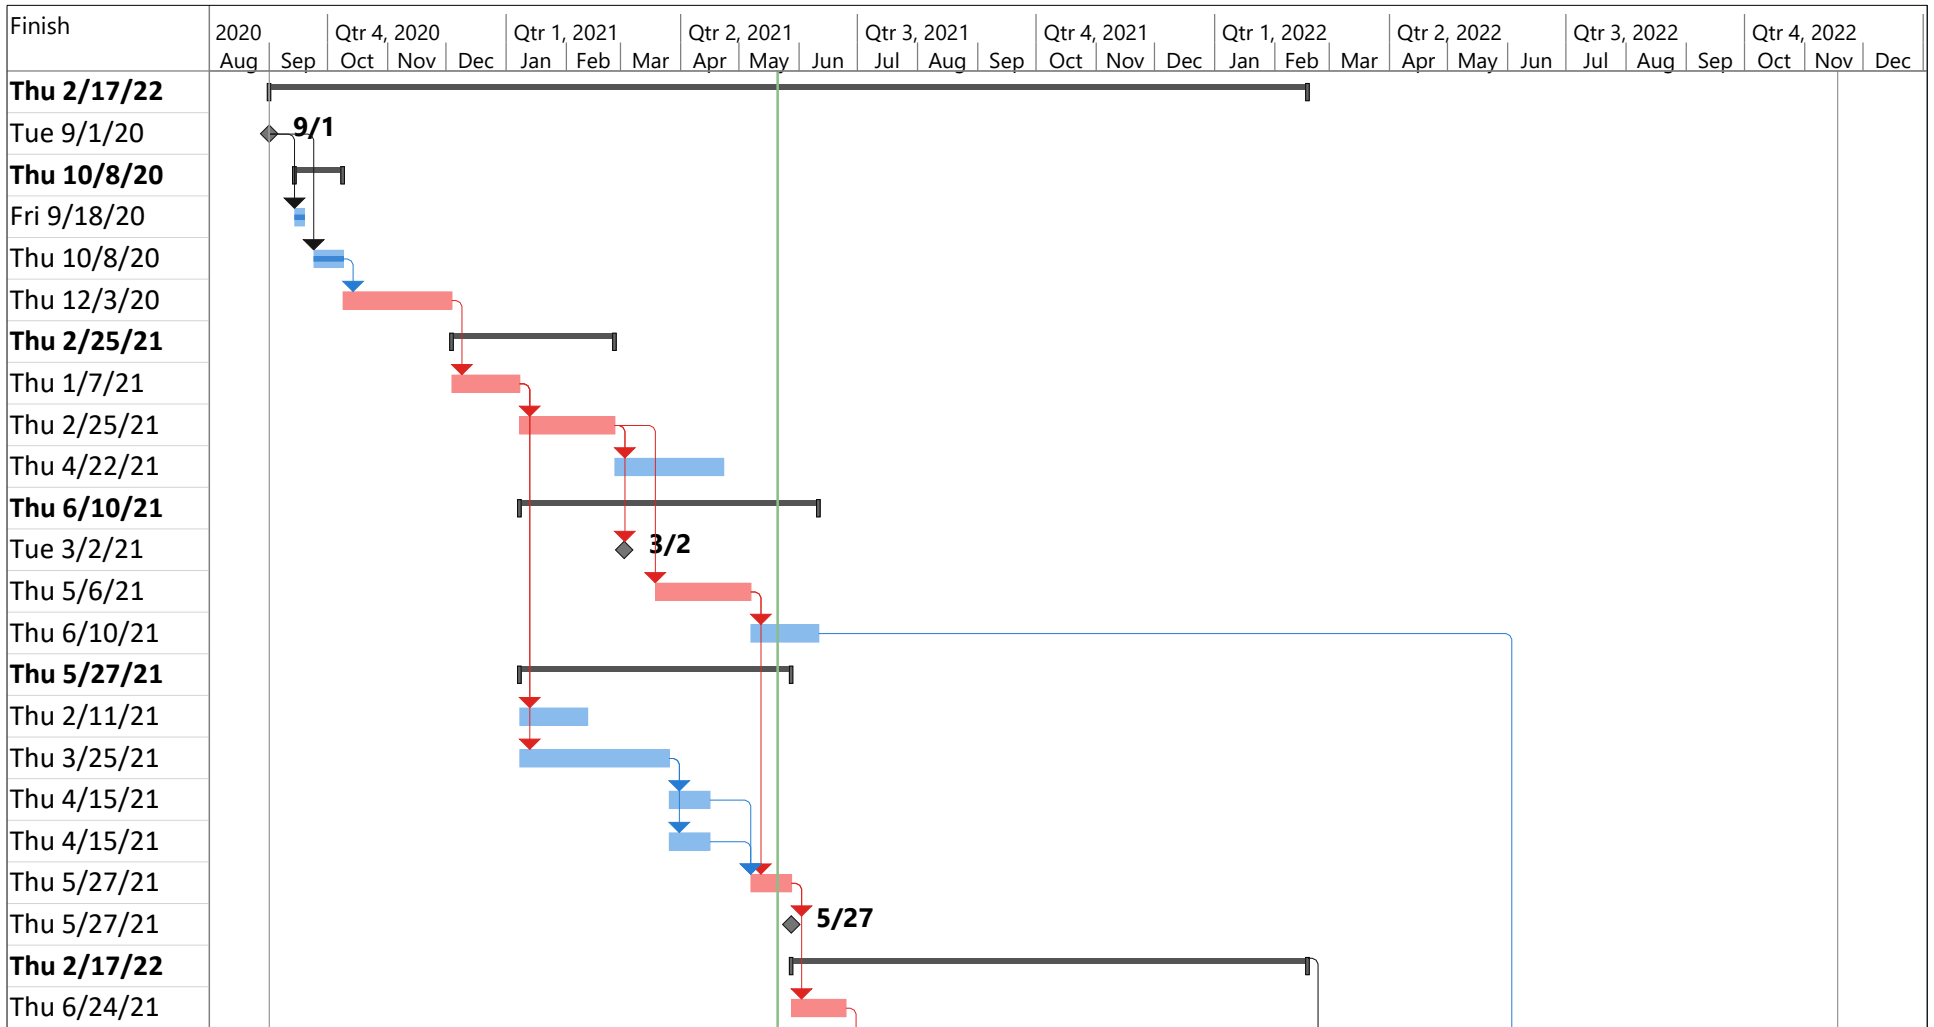


Project: Implementation Schedu
Date: Fri 5/21/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

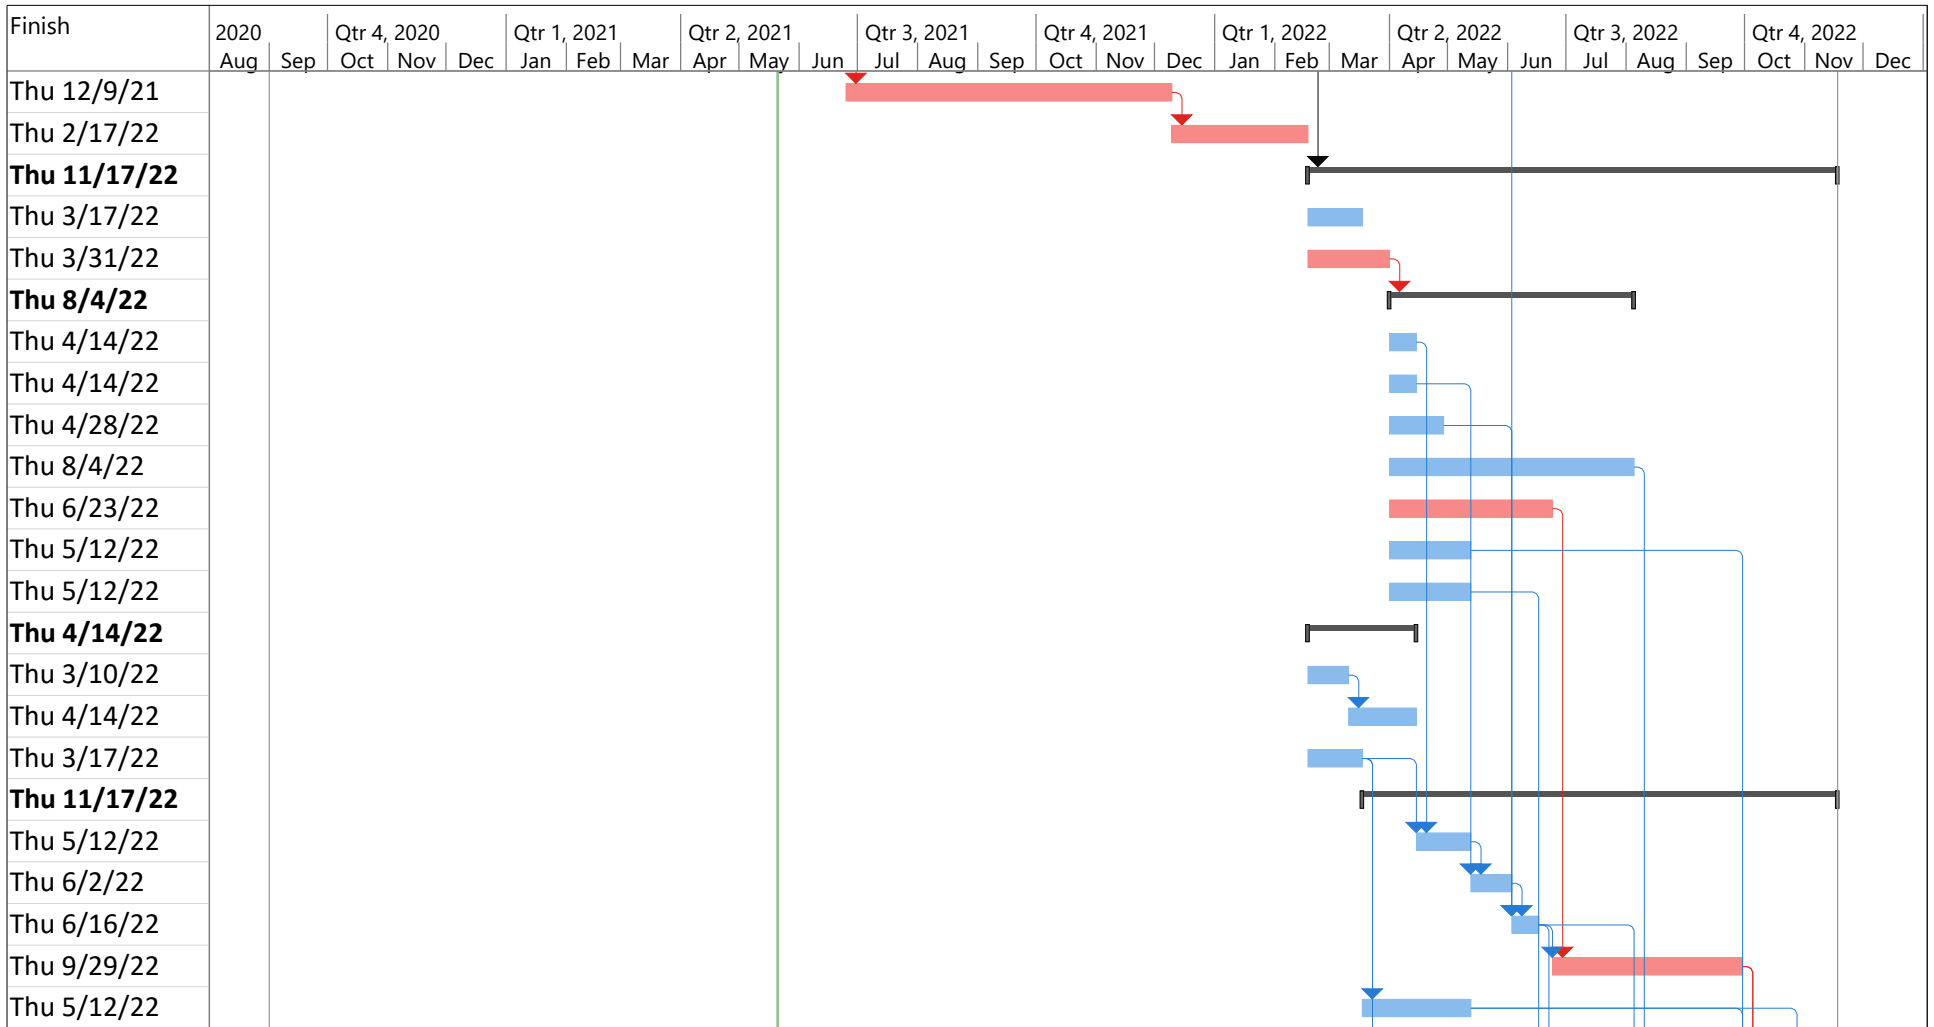

Project: Implementation Schedu
Date: Fri 5/21/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

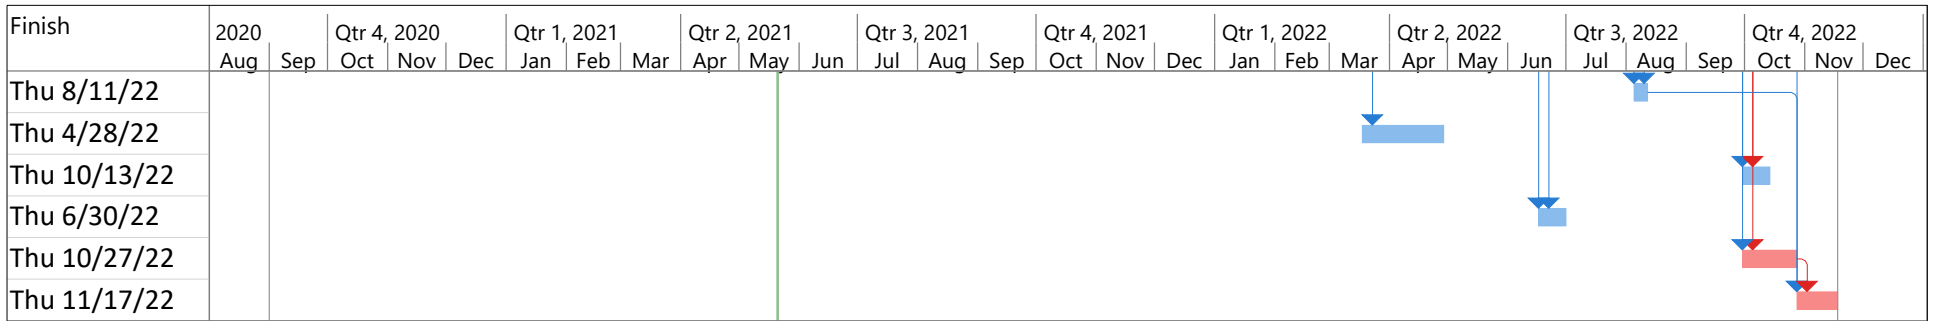

Project: Implementation Schedu Date: Fri 5/21/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	
